


ID	Task Mode	Task Name	Duration	Start	Finish	Predecessors	ul 12, '26	Jul 19, '26	Jul 26, '26	Aug 2, '26	Aug 9, '26	Aug 16, '26	Aug 23, '26	Aug 30, '26	Sep 6, '26	Sep 13, '26	Sep 20, '26	Sep 27, '26	Oct 4, '26	
1		Gilmore and Thompson Street Improvements	108.5 days	Tue 5/12/26	Fri 10/9/26															
2	★	Notice of Award	1 day	Tue 5/12/26	Tue 5/12/26															
3	★	Contracts	20 days	Tue 5/12/26	Mon 6/8/26	2SS														
4	★	Preconstruction Conference																		
5	★	Submittals																		
6		Gilmore/Pioneer/Thompson/Morrow	64.5 days	Mon 7/13/26	Fri 10/9/26															
7	★	Notice to Proceed	1 day	Mon 7/13/26	Mon 7/13/26															
8	★	Traffic Control	1 day	Tue 7/14/26	Tue 7/14/26	7														
9	★	Lower Existing Utilities	2 days	Wed 7/15/26	Thu 7/16/26	8														
10	★	Demo Work	5 days	Fri 7/17/26	Thu 7/23/26	9														
11	★	Asphalt Grinding	1 day	Fri 7/24/26	Fri 7/24/26	10														
12	★	8" PVC Gravity Sewer Line	7 days	Mon 7/27/26	Tue 8/4/26	11														
13	★	Sewer Services	7 days	Wed 8/5/26	Thu 8/13/26	12														
14	★	Sewer Testing/Cleaning	2 days	Fri 8/14/26	Mon 8/17/26	13														
15	★	8" PVC Water Line	6 days	Tue 8/18/26	Tue 8/25/26	14														
16	★	Water Services	7 days	Wed 8/26/26	Thu 9/3/26	15														
17	★	Fire Hydrants	1 day	Wed 8/26/26	Wed 8/26/26	15														
18	★	Water Testing	3 days	Thu 8/27/26	Mon 8/31/26	17														
19	★	Water Connections to Existing System	3 days	Tue 9/1/26	Thu 9/3/26	18														
20	★	Storm System	3 days	Fri 9/4/26	Tue 9/8/26	19														
21	★	Subgrade Roadway	4 days	Wed 9/9/26	Mon 9/14/26	20														
22	★	Aggregate Base Rock	5 days	Tue 9/15/26	Mon 9/21/26	21														
23	★	Curb and Gutter	3 days	Tue 9/22/26	Thu 9/24/26	22														
24	★	Sidewalks/Driveways	2 days	Fri 9/25/26	Mon 9/28/26	23														
25	★	Finalize Aggregate Base Rock	1 day	Tue 9/29/26	Tue 9/29/26	24														
26	★	HMA Paving	2 days	Wed 9/30/26	Thu 10/1/26	25														
27	★	Pavement Striping & Marking	2 days	Fri 10/2/26	Mon 10/5/26	26														
28	★	Cleaning/Punchlist	3 days	Tue 10/6/26	Thu 10/8/26	27														
29		Linden Way Alley	3.5 days	Tue 10/6/26	Fri 10/9/26															
30	★	Scarify/Subgrade	1.5 days	Tue 10/6/26	Wed 10/7/26	27														
31	★	Aggregate Base Rock	2 days	Wed 10/7/26	Fri 10/9/26	30														
32		Willow Street Improvements	8 days	Tue 9/22/26	Thu 10/1/26															
33	★	Move Equipment In	1 day	Tue 9/22/26	Tue 9/22/26	22														
34	★	Traffic Control	1 day	Wed 9/23/26	Wed 9/23/26	33														
35	★	Demo/Sawcut	1 day	Thu 9/24/26	Thu 9/24/26	34														
36	★	Storm System	2 days	Fri 9/25/26	Mon 9/28/26	35														
37	★	Prep Patch	1 day	Tue 9/29/26	Tue 9/29/26	36														
38	★	Concrete Curb	1 day	Wed 9/30/26	Wed 9/30/26	37														
39	★	HMA Patching	1 day	Thu 10/1/26	Thu 10/1/26	38														

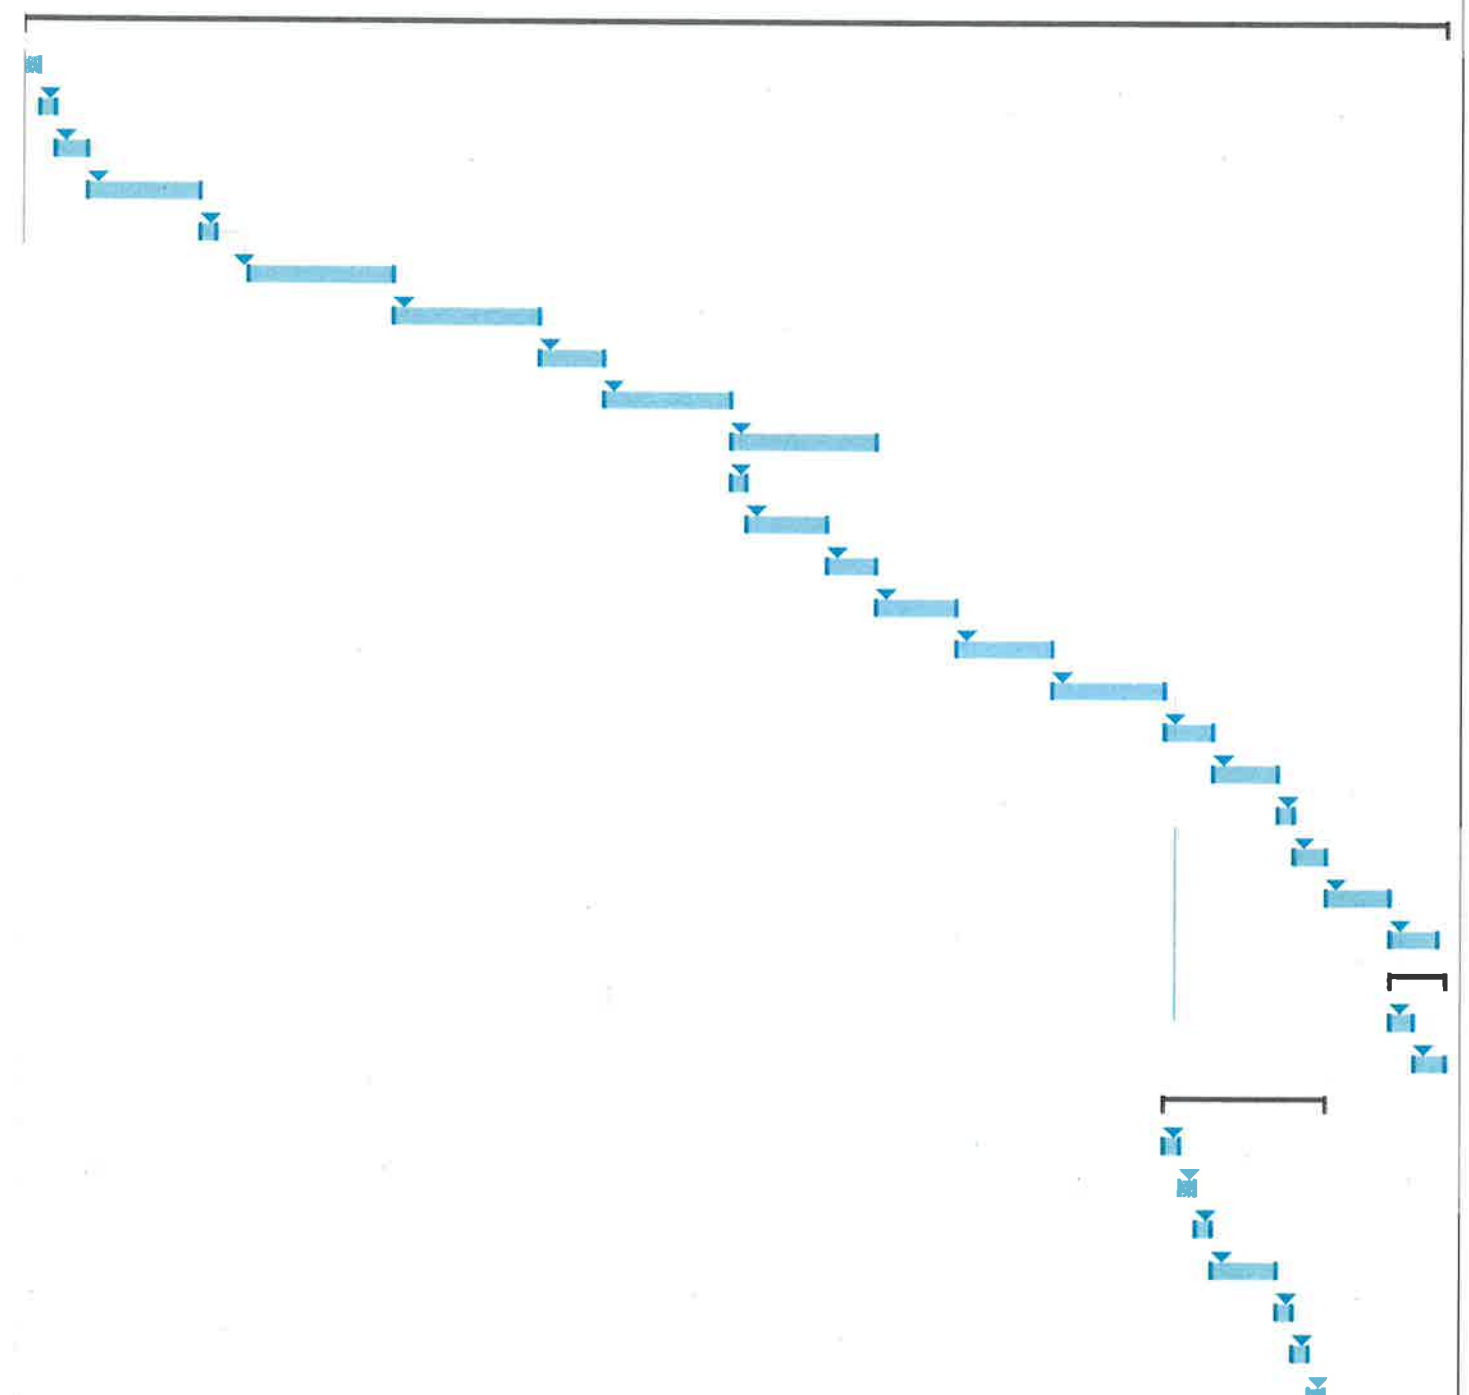

Project: Pre-Con 06.19.2026 Date: Fri 6/19/26	Task		Project Summary		Manual Task		Start-only		Finish-only		External Tasks		External Milestone		Deadline		Progress		Manual Progress	
	Split		Inactive Task		Duration-only		Start-only		Finish-only		External Tasks		External Milestone		Deadline		Progress		Manual Progress	
	Milestone		Inactive Milestone		Manual Summary Rollup		Start-only		Finish-only		External Tasks		External Milestone		Deadline		Progress		Manual Progress	
	Summary		Inactive Summary		Manual Summary		Start-only		Finish-only		External Tasks		External Milestone		Deadline		Progress		Manual Progress	
